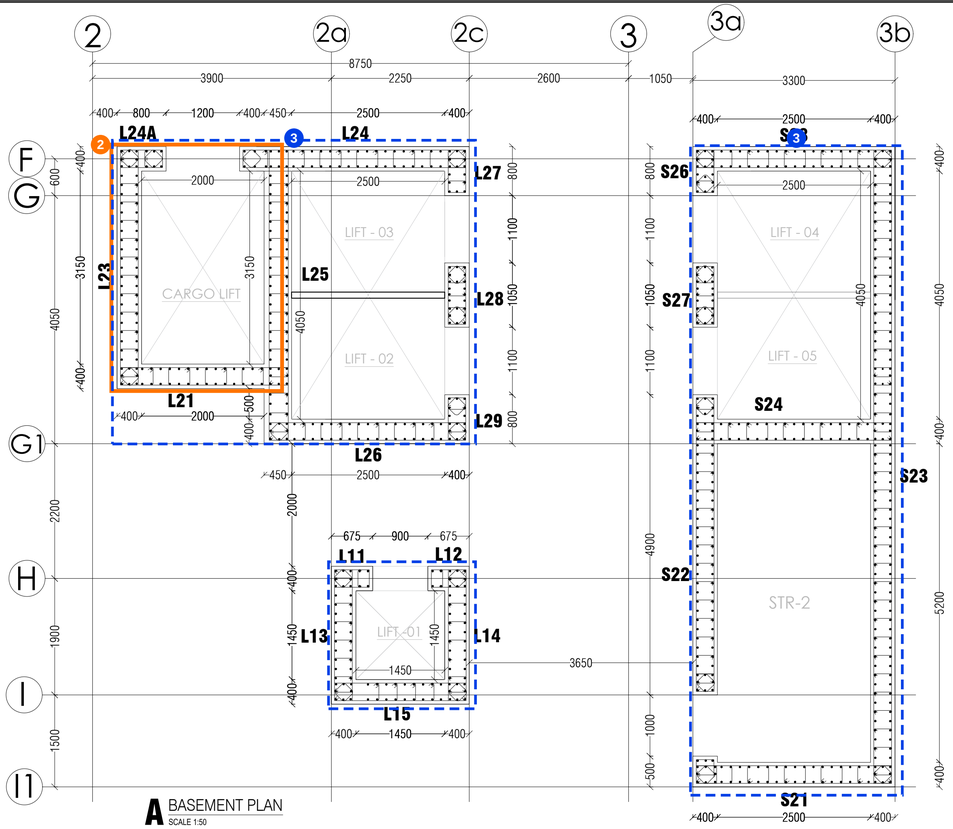

A BASEMENT PLAN
SCALE 1:50

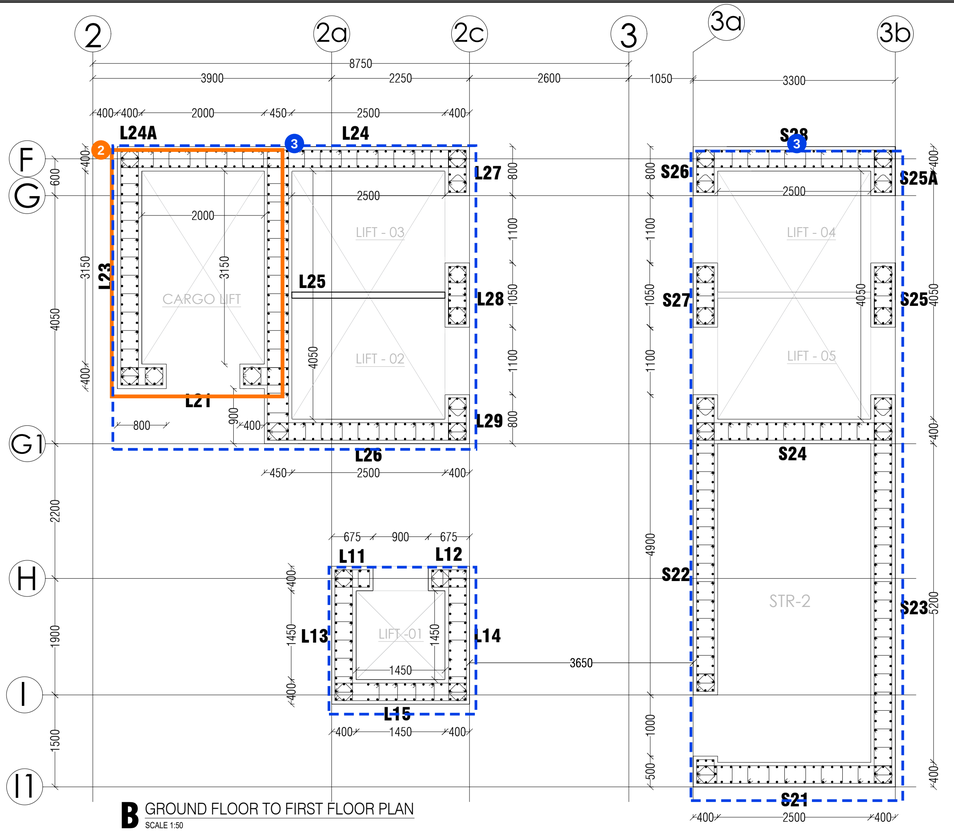

B GROUND FLOOR TO FIRST FLOOR PLAN
SCALE 1:50

NOTE: Contractor to take approval of the consultant for the workshop drawings of Columns & Walls reinforcement details, prepared in accordance to section 18.10 of ACI 318-19 before execution of works.

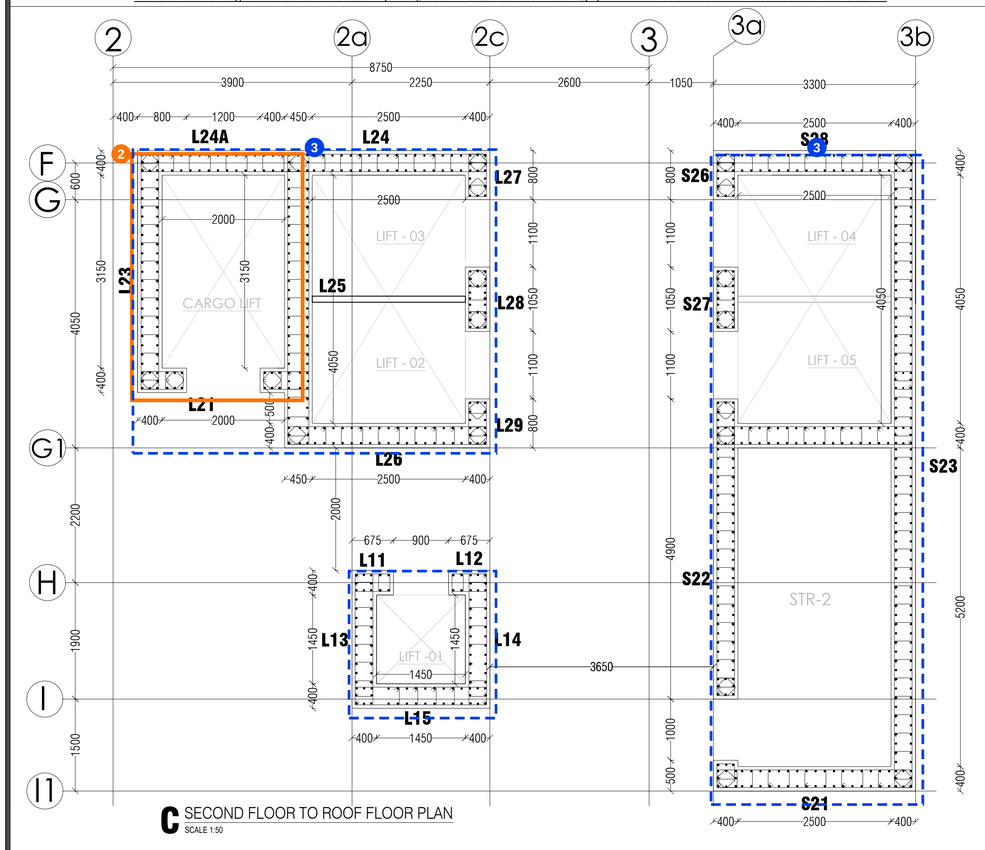

C SECOND FLOOR TO ROOF FLOOR PLAN
SCALE 1:50

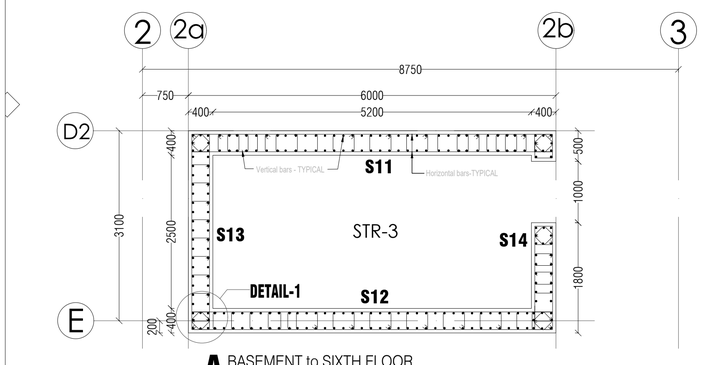

A BASEMENT to SIXTH FLOOR
SCALE 1:50



TYPICAL SPANDRAL DETAIL ABOVE DOOR OPENING

RETAINING WALLS= 300MM THICK TYPICAL DETAIL



1 TYPICAL DETAIL AT CORNERS/EDGES
REINF : 8T25/8T20
: T10@150 C/C - TYP.



2 TYPICAL CORNER DETAIL
REINF : 8T20/8T16
: T10@200 C/C - TYP.
TYPICAL CORNER DETAILS FOR RETAINING WALL

RFI DS-STR-ASEC-RFI-CIVIL-003 (S-110)

2 Cargo lift entrance does not match between sheets - full detail required for execution.

3 Lift/core walls: approval requested to proceed with casting without lift shop drawings.

SCHEDULE OF SHEAR WALLS

WALL = S11, S12, S13, S14 = 400MM THK.
2-T25@150c/c-(V) = RAFT TO 3RD FLOOR
2L-T10@125c/c-(H) = RAFT TO 3RD FLOOR
2-T20@150c/c-(V) = 4TH FLOOR TO ROOF
2L-T10@150c/c-(H) = 4TH FLOOR TO ROOF
Boundary Zone for S11 & S12: 1.6m from left and right ends, for S13 & S14: 1.0m from left and right ends.

WALL = S25(GF Only) & S26 - 400MM THK.
2-T32@100c/c-(V) = RAFT TO ROOF
2L-T12@100c/c-(H) = RAFT TO ROOF
Boundary Zone length: 0.5m from left and right ends.

WALL = S27 - 400MM THK.
2-T32@150c/c-(V) = RAFT TO ROOF
2L-T12@100c/c-(H) = RAFT TO ROOF
Boundary Zone length: 0.5m from left and right ends.

WALL = S21 & S28 - 400MM THK.
2-T25@150c/c-(V) = RAFT TO 1ST FLOOR
2L-T12@150c/c-(H) = RAFT TO 1ST FLOOR
2-T20@150c/c-(V) = 2ND FLOOR TO ROOF
2L-T12@150c/c-(H) = 2ND FLOOR TO ROOF
Boundary Zone: 1.3m from left and right ends upto 3rd floor then 0.6m upto roof floor.

WALL = S22,S23 & S24 - 400MM THK.
2-T20@150c/c-(V) = RAFT TO ROOF
2L-T12@125c/c-(H) = RAFT TO ROOF
Boundary Zone: 1.5m from left and right ends upto 3rd floor then 0.6m upto roof floor.

WALL = S25A(GF Only)- 400MM THK.
2-T32@ 70 c/c-(V), T12@125 c/c(H) & Ties.

WALL = L21- 400MM THK.
2-T32@150c/c-(V) = RAFT TO 1ST FLOOR
2L-T12@150c/c-(H) = RAFT TO 1ST FLOOR
2-T25@150c/c-(V) = 2ND FLOOR TO 3RD FLOOR
2L-T12@150c/c-(H) = 2ND FLOOR TO 3RD FLOOR
2-T20@150c/c-(V) = 4TH FLOOR TO ROOF
2L-T10@150c/c-(H) = 4TH FLOOR TO ROOF
Boundary Zone: 0.75m from left and right ends upto roof floor.

WALL = L23 ,L24A , L24 , L25 , L26 - 400MM THK.
2-T25@150c/c-(V) = RAFT TO 1ST FLOOR
2L-T10@150c/c-(H) = RAFT TO 1ST FLOOR
2-T20@150c/c-(V) = 2ND FLOOR TO ROOF
2L-T10@150c/c-(H) = 2ND FLOOR TO ROOF
Boundary Zone for L23 & L24+L24A: 1.4m from left and right ends, for others: 0.9m from left and right ends.

WALL = L27 , L29- 400MM THK.
2-T32@150c/c-(V) = RAFT TO 1ST FLOOR
2L-T12@125c/c-(H) = RAFT TO 1ST FLOOR
2-T25@150c/c-(V) = 2ND FLOOR TO ROOF
2L-T12@150c/c-(H) = 2ND FLOOR TO ROOF
Boundary Zone length: 0.5m from left and right ends.

WALL = L28 - 400MM THK.
2-T25@150c/c-(V) = RAFT TO 1ST FLOOR
2L-T12@150c/c-(H) = RAFT TO 1ST FLOOR
2-T20@150c/c-(V) = 2ND FLOOR TO ROOF
2L-T10@120c/c-(H) = 2ND FLOOR TO ROOF
Boundary Zone length: 0.5m from left and right ends.

WALL = L11 , L12 - 400MM THK.
2-T25@150c/c-(V) = RAFT TO ROOF
2L-T10@150c/c-(H) = RAFT TO ROOF
Boundary Zone length: Full length.

WALL = L13 , L14 , L15 - 400MM THK.
2-T20@150c/c-(V) = RAFT TO ROOF
2L-T10@150c/c-(H) = RAFT TO ROOF
Boundary Zone length: 0.6m from left and right ends.

NOTE: 1) T10@300c/c-HOOK - TYPICAL FOR ALL WALLS
2) In boundary zone lengths at ends of walls all vertical wall reinforcement bars are to be tied with T10 bars as guided by section 18-10 of ACI 318-19.
Consultants prior approval be obtained by the contractor of their workshop drawings before execution of works.

NOTE :

(1) THIS DRAWING IS THE PROPERTY OF :
AL SARAYA ENGINEERING CONSULTANT
P.O.BOX: 49162, DUBAI, U.A.E.
IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:
1. fcu = 50 N/mm²
2. fy = 460 N/mm²

* ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

NOTE: 34% OPC + 66% GGBS + 5% MICRO SILICA

LEGEND:
- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

CIVIL ENGINEERING DEPARTMENT
Drawing has been reviewed for compliance with the Regulations and is:
NO OBJECTION
Permit Engineer: ..... Date .....

Subject to compliance with designed codes, approved architectural and structural, EHS regulation and Dubai civil defence requirments

AL SARAYA ENGINEERING CONSULTANTS
P.O.Box 49162 Tel.: 04-3350084
Dubai - U.A.E. Fax: 04-3350087

REVISIONS:

NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER:
B M L INVESTMENT LLC

OWNER:
DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT:
AL SARAYA ENGINEERING CONSULTANTS
السرايا للاستشارات الهندسية
Architects , Engineers , Planners P.O.Box - 49162 , DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT
CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, API World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101 PLOT: 1010619

PROJECT:
PROPOSED B+G+7+R HOTEL
ON PLOT NO.DIA-WE-0032(1010619),
NAKHLAT DEIRA-101,DUBAI

DRG. TITLE:
SHEAR WALL DETAILS

SCALE:	1:150/A1	KEY:	–
APPROVED BY:	SJ	DRAWN BY:	SPP
DATE:	--	PLOTTED ON:	–
PRELIMINARY	FINAL	ADDITION	REVISION
ISSUED FOR:	—		

JOB NO. : 624

DRG. NO.: S-110

REV. 00

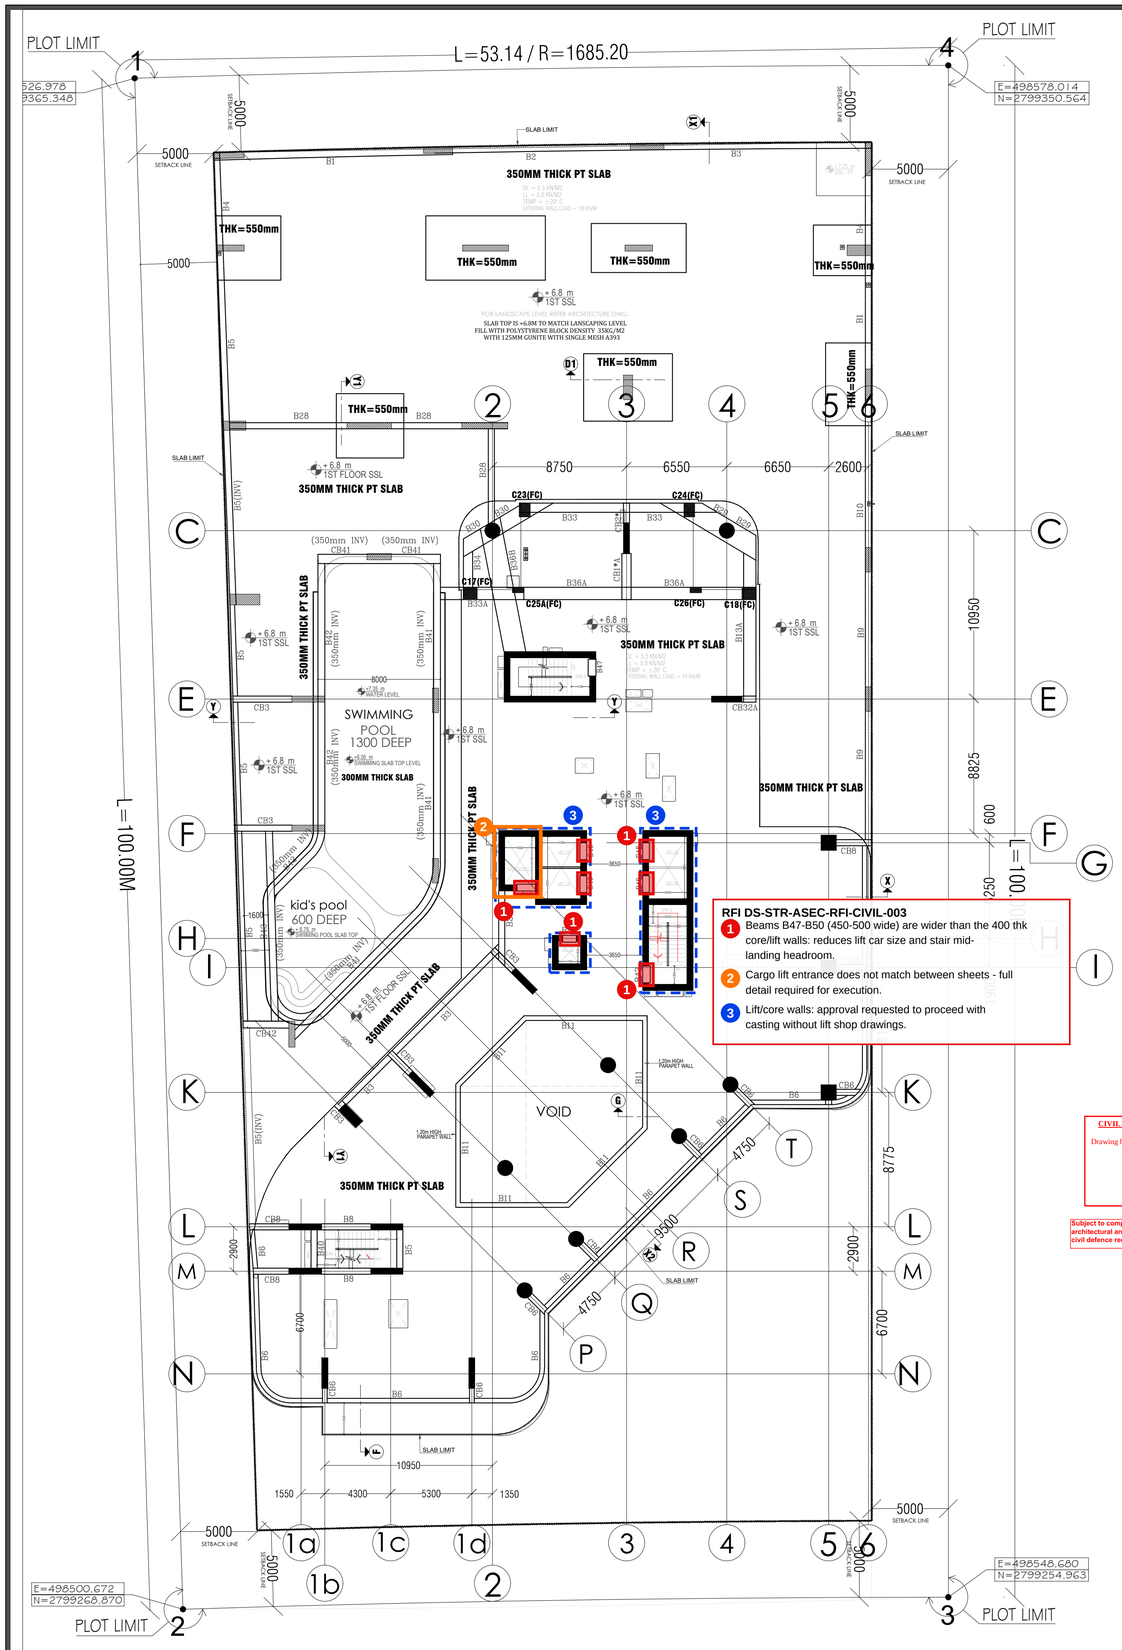

RFI DS-STR-ASEC-RFI-CIVIL-003

1. Beams B47-B50 (450-500 wide) are wider than the 400 thk core/lift walls: reduces lift car size and stair mid-landing headroom.
2. Cargo lift entrance does not match between sheets - full detail required for execution.
3. Lift/core walls: approval requested to proceed with casting without lift shop drawings.

CIVIL ENGINEERING DEPARTMENT

Drawing has been **reviewed** for compliance with the Regulations and is:

NO OBJECTION

Permit Engineer:

Subject to compliance with designed codes, approved architectural and structural, EHS regulation and Dubai civil defence requirments

SCHEDULE OF BEAMS

TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
CB1A	600	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '*' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.

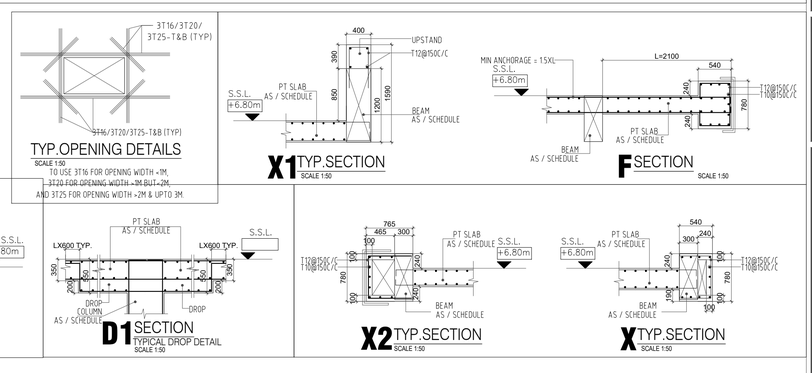

NOTE :

(1) THIS DRAWING IS THE PROPERTY OF : AL SARAYA ENGINEERING CONSULTANT P.O.BOX: 49162, DUBAI, U.A.E. IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:

1. fcu = 50 N/mm²
2. fy = 460 N/mm²

* ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:

- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES :

- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG
- WHEREVER NECESSARY BEAM DEPTH ARE INCREASED, MODIFIED OR DOMESTRED TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIPHERAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS OR DRGS.

AL SARAYA ENGINEERING CONSULTANTS
P.O.Box 49162 Tel.: 04-3350084
Dubai - U.A.E. Fax: 04-3350087

REVISIONS:		
NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER: B M L INVESTMENT LLC

OWNER: DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT: AL SARAYA ENGINEERING CONSULTANTS السرايا للإستشارات الهندسية
Architects , Engineers , Planners P.O.Box - 49162 , DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT: CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, API World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101	PLOT: 1010619
PROJECT: PROPOSED B+G+7+R HOTEL ON PLOT NO.DIA-WE-0032(1010619), NAKHLAT DEIRA-101,DUBAI	
DRG. TITLE: 1ST FLOOR FRAMING	
SCALE: 1:150/A1	KEY: –
APPROVED BY: SJ	DRAWN BY: SPP
DATE: --	PLOTTED ON: –
PRELIMINARY / FINAL / ADDITION / REVISION	
ISSUED FOR: –	
JOB NO. : 624	
DRG. NO.: S-302	REV. 00

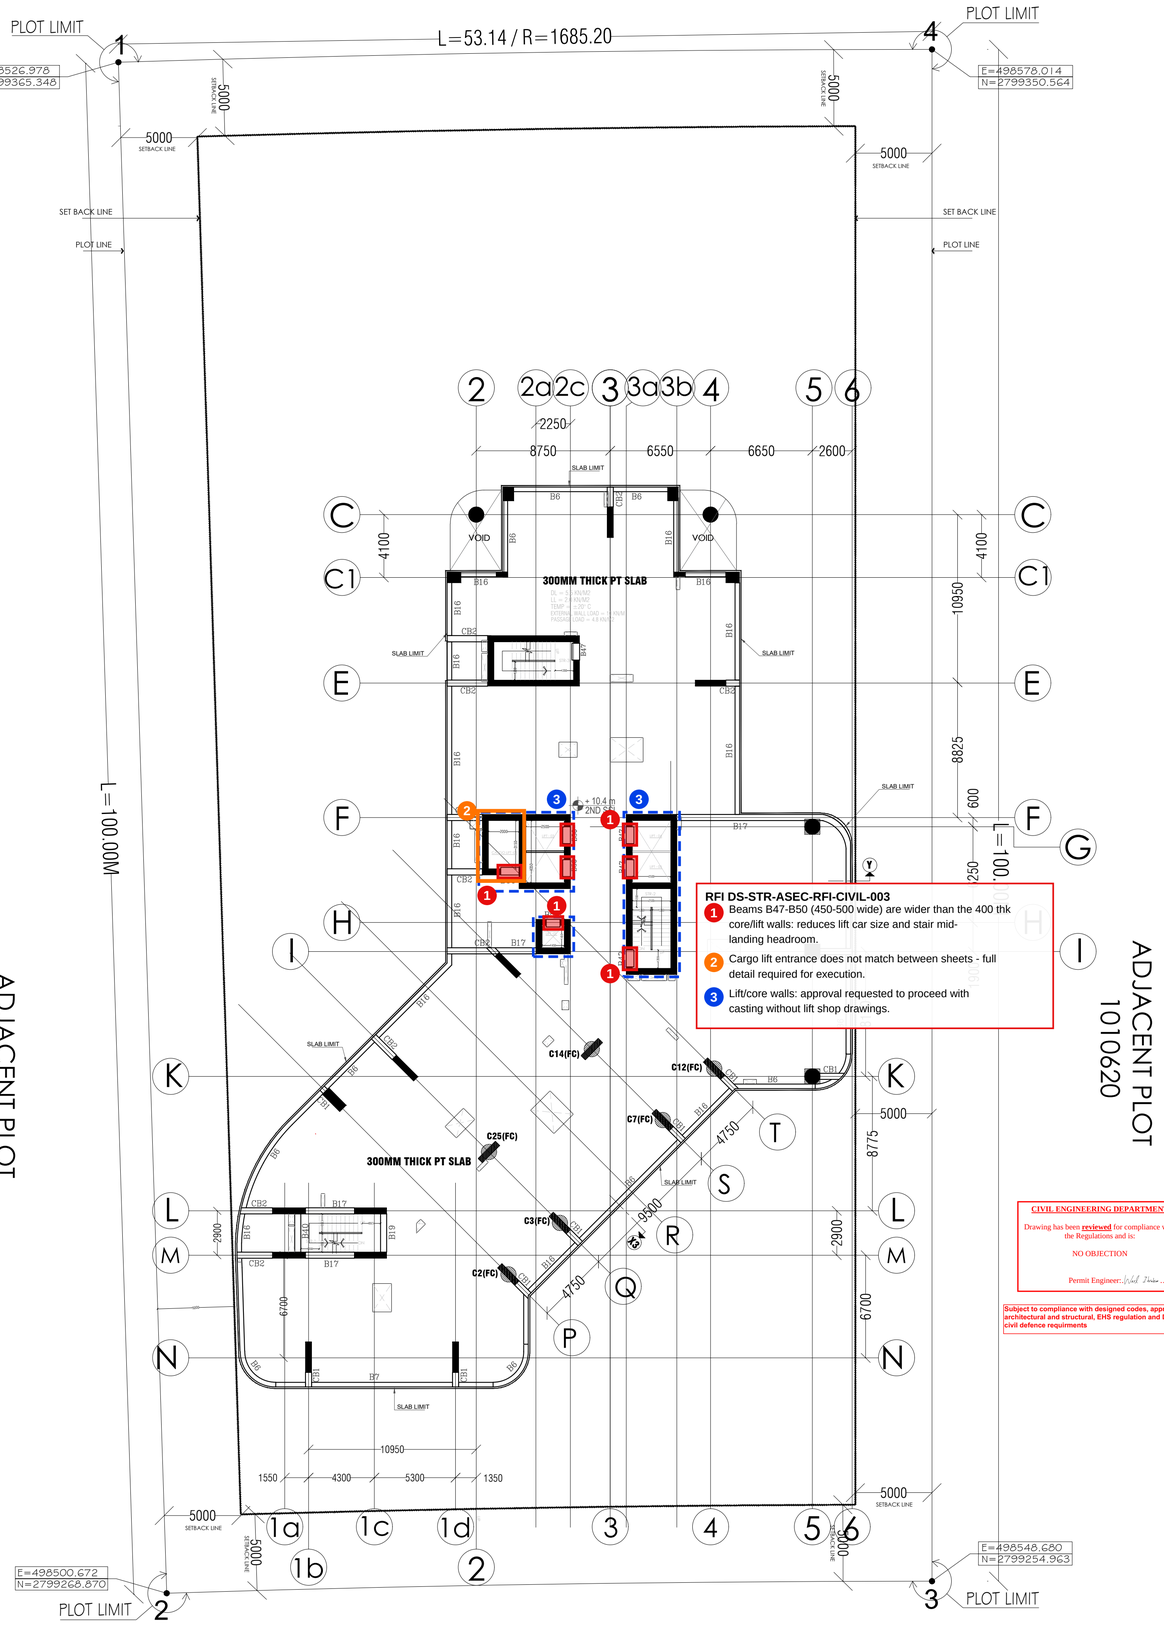

2ND FLOOR FRAMING LAYOUT

SCHEDULE OF BEAMS

TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
CB1A	600	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '•' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.







NOTE :

(1) THIS DRAWING IS THE PROPERTY OF : AL SARAYA ENGINEERING CONSULTANT P.O.BOX: 49162, DUBAI, U.A.E. IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:
1. fcu = 50 N/mm²
2. fy = 460 N/mm²
* ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:
- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES :
- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG
- WHEREVER NECESSARY BEAM DEPTH ARE INCREASED, INVERTED OR DOWNSTAND TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIMETERAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS, OR DROS.

AL SARAYA ENGINEERING CONSULTANTS
P.O.Box 49162 Tel.: 04-3350084
Dubai - U.A.E. Fax: 04-3350087

REVISIONS:

NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03		
04		

DEVELOPER: B M L INVESTMENT LLC

OWNER: DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT: AL SARAYA ENGINEERING CONSULTANTS السرايا للاستشارات الهندسية
Architects , Engineers , Planners P.O.Box - 49162 , DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT: CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, API World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101 PLOT: 1010619

PROJECT: PROPOSED B+G+7+R HOTEL ON PLOT NO.DIA-WE-0032(1010619), NAKHLAT DEIRA-101,DUBAI

DRG. TITLE: 2ND FLOOR FRAMING

SCALE:	1:150/A1	KEY:	–
APPROVED BY:	SJ	DRAWN BY:	SPP
DATE:	--	PLOTTED ON:	–
PRELIMINARY	FINAL	ADDITION	REVISION
ISSUED FOR:	–		

JOB NO. : 624

DRG. NO.: S-303 REV. 00

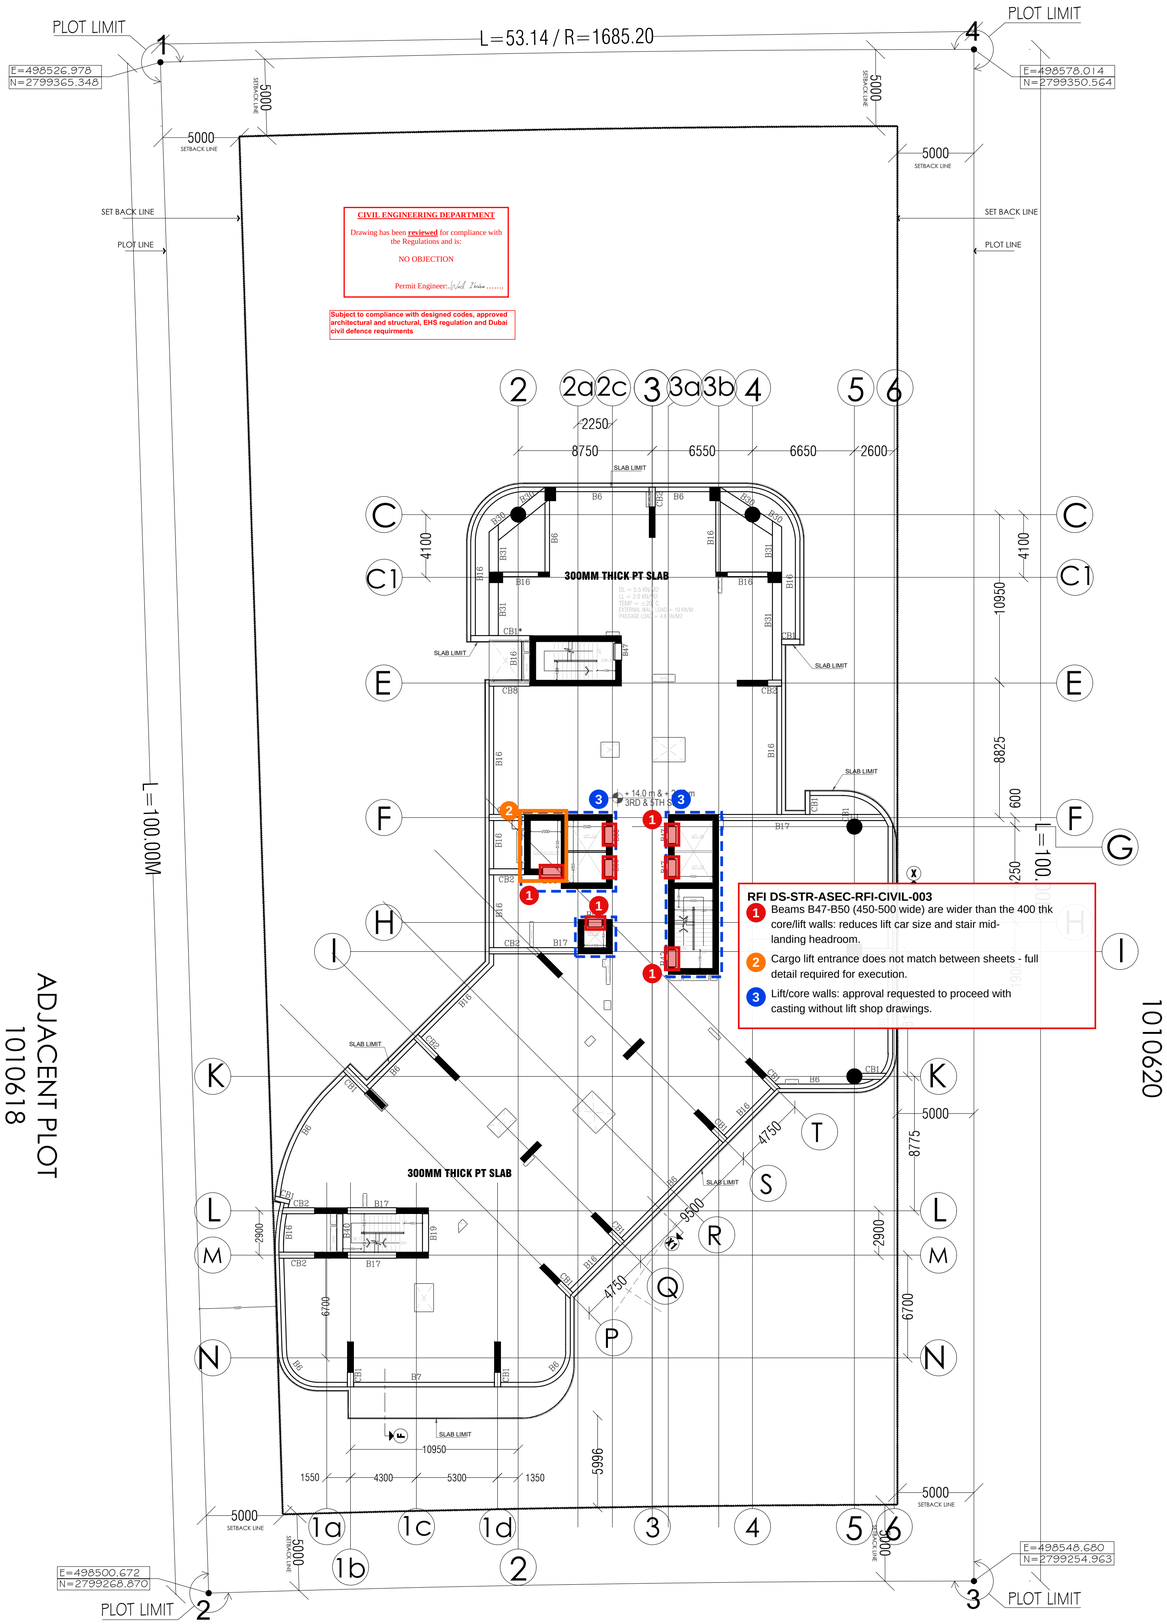

3RD & 5TH FLOOR FRAMING LAYOUT

SCHEDULE OF BEAMS

TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
CB1A	600	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '•' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.



X1 TYP.SECTION
SCALE 1:50



X TYP.SECTION
SCALE 1:50



F SECTION
SCALE 1:50



TYP.OPENING DETAILS
SCALE 1:50
TO USE 3T16 FOR OPENING WIDTH <1M,
3T20 FOR OPENING WIDTH >1M BUT<2M,
AND 3T25 FOR OPENING WIDTH >2M & UPTO 3M

NOTE :

(1) THIS DRAWING IS THE PROPERTY OF : AL SARAYA ENGINEERING CONSULTANT P.O.BOX: 49162, DUBAI, U.A.E. IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:
1. fcu = 50 N/mm²
2. fy = 460 N/mm²
* ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:
- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES :
- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG
- WHEREVER NECESSARY BEAM DEPTH ARE INCREASED, INVERTED OR DOWNSTAND TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIMPHERAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS OR DROS.

AL SARAYA ENGINEERING CONSULTANTS
P.O.Box 49162 Tel.: 04-3350084
Dubai - U.A.E. Fax: 04-3350087

REVISIONS:		
NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER: B M L INVESTMENT LLC

OWNER: DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT:
AL SARAYA ENGINEERING CONSULTANTS
السرايا للإستشارات الهندسية
Architects , Engineers , Planners P.O.Box - 49162 , DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT
CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, API World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101 PLOT: 1010619

PROJECT:
PROPOSED B+G+7+R HOTEL ON PLOT NO.DIA-WE-0032(1010619), NAKHLAT DEIRA-101,DUBAI

DRG. TITLE:
3RD & 5TH FLOOR FRAMING

SCALE:	1:150/A1	KEY:	–
APPROVED BY:	SJ	DRAWN BY:	SPP
DATE:	--	PLOTTED ON:	–
PRELIMINARY	FINAL	ADDITION	REVISION
ISSUED FOR:	—		

JOB NO. : 624

DRG. NO.: S-304 REV. 00

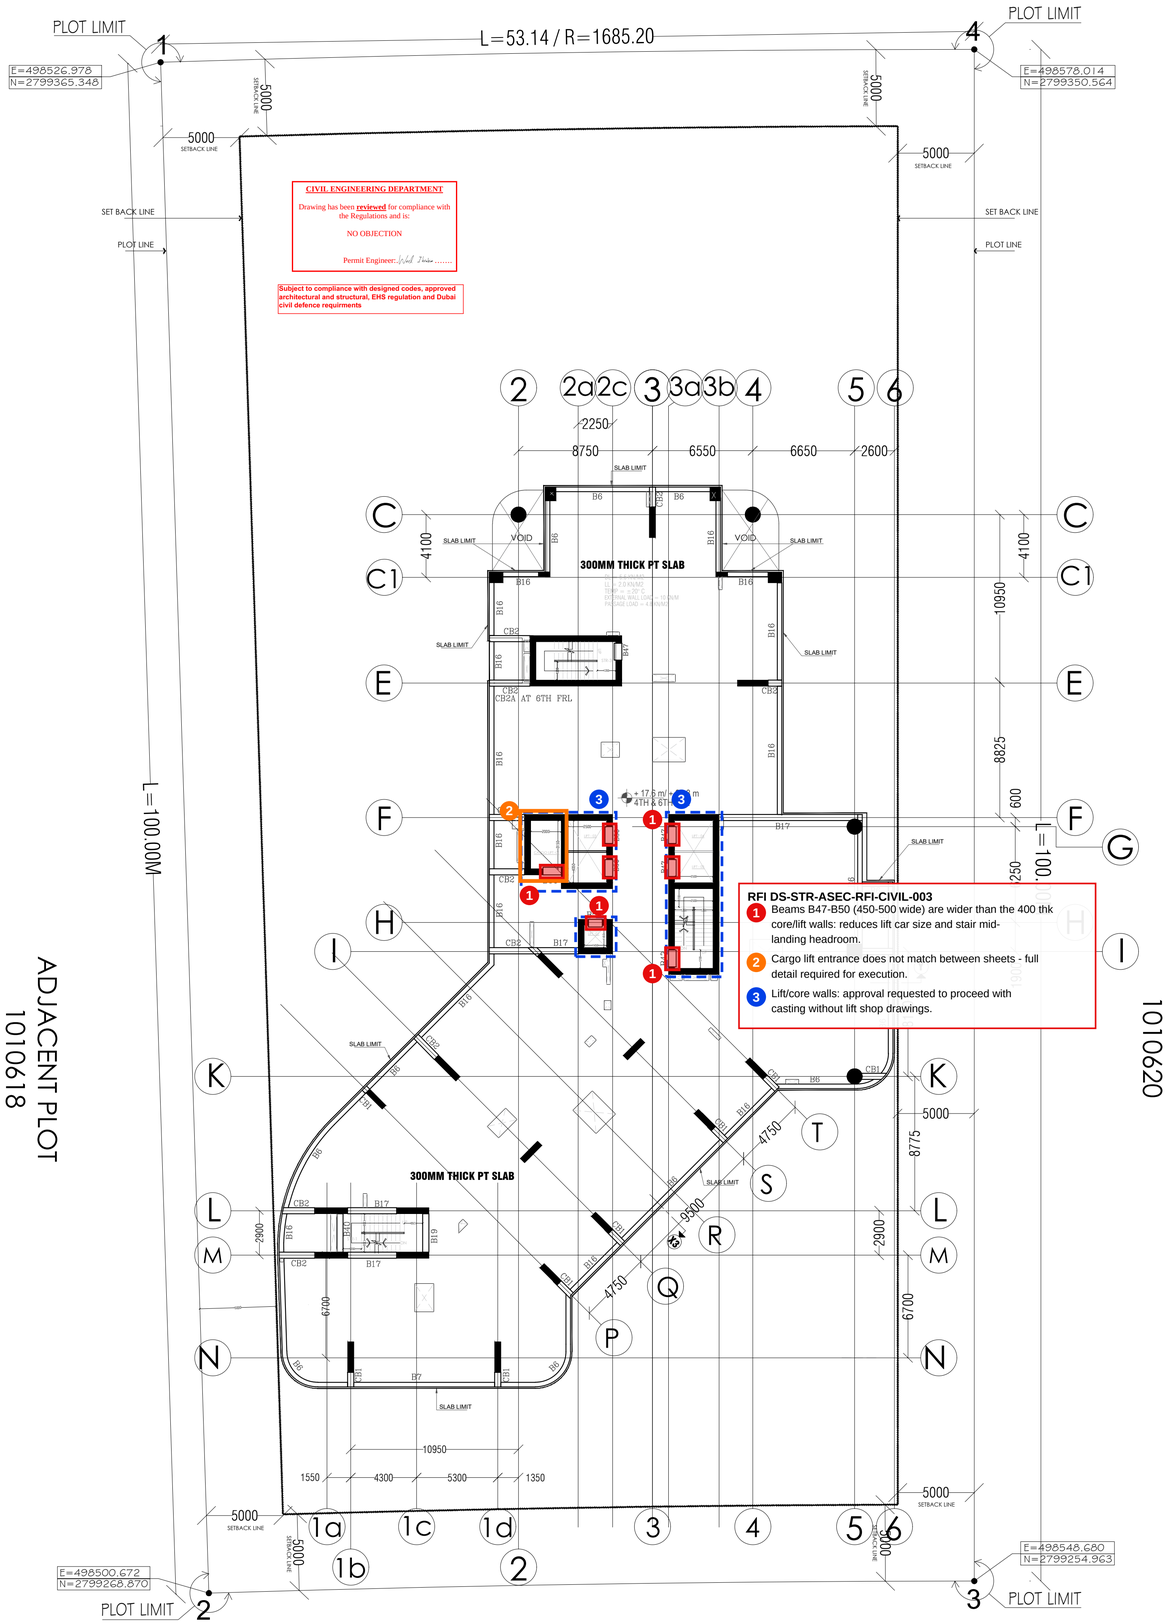

4TH & 6th FLOOR FRAMING LAYOUT

SCHEDULE OF BEAMS

TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
1 B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
CB1A	600	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '*' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.



X3 TYP.SECTION SCALE 1:50



Y TYP.SECTION SCALE 1:50



TYP.OPENING DETAILS SCALE 1:50
TO USE 3T16 FOR OPENING WIDTH <1M.
3T20 FOR OPENING WIDTH >1M BUT<2M,
AND 3T25 FOR OPENING WIDTH >2M & UPTO 3M.

NOTE :

(1) THIS DRAWING IS THE PROPERTY OF :
AL SARAYA ENGINEERING CONSULTANT
P.O.BOX: 49162, DUBAI, U.A.E.
IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:
1. fcu = 50 N/mm²
2. fy = 460 N/mm²
* ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:
- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES.:
- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG
- WHEREVER NECESSARY BEAM DEPTH ARE INCREASED, INVERTED OR DOWNSTAND TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIMETERAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS OR DRGS.

AL SARAYA ENGINEERING CONSULTANTS
P.O.Box 49162 Tel.: 04-3350084
Dubai - U.A.E. Fax: 04-3350087

REVISIONS:

NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER: B M L INVESTMENT LLC

OWNER: DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT: AL SARAYA ENGINEERING CONSULTANTS السرايا للإستشارات الهندسية
Architects , Engineers , Planners P.O.Box - 49162 , DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT: CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125706, Office 2001 & 2002, API World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101 PLOT: 1010619

PROJECT:
PROPOSED B+G+7+R HOTEL
ON PLOT NO.DIA-WE-0032(1010619),
NAKHLAT DEIRA-101,DUBAI

DRG. TITLE:
4TH & 6TH FLOOR FRAMING

SCALE:	1:150/A1	KEY:	–
APPROVED BY:	SJ	DRAWN BY:	SPP
DATE:	--	PLOTTED ON:	–

PRELIMINARY | FINAL | ADDITION | REVISION

ISSUED FOR: –

JOB NO. : 624

DRG. NO.: S-305 REV. 00

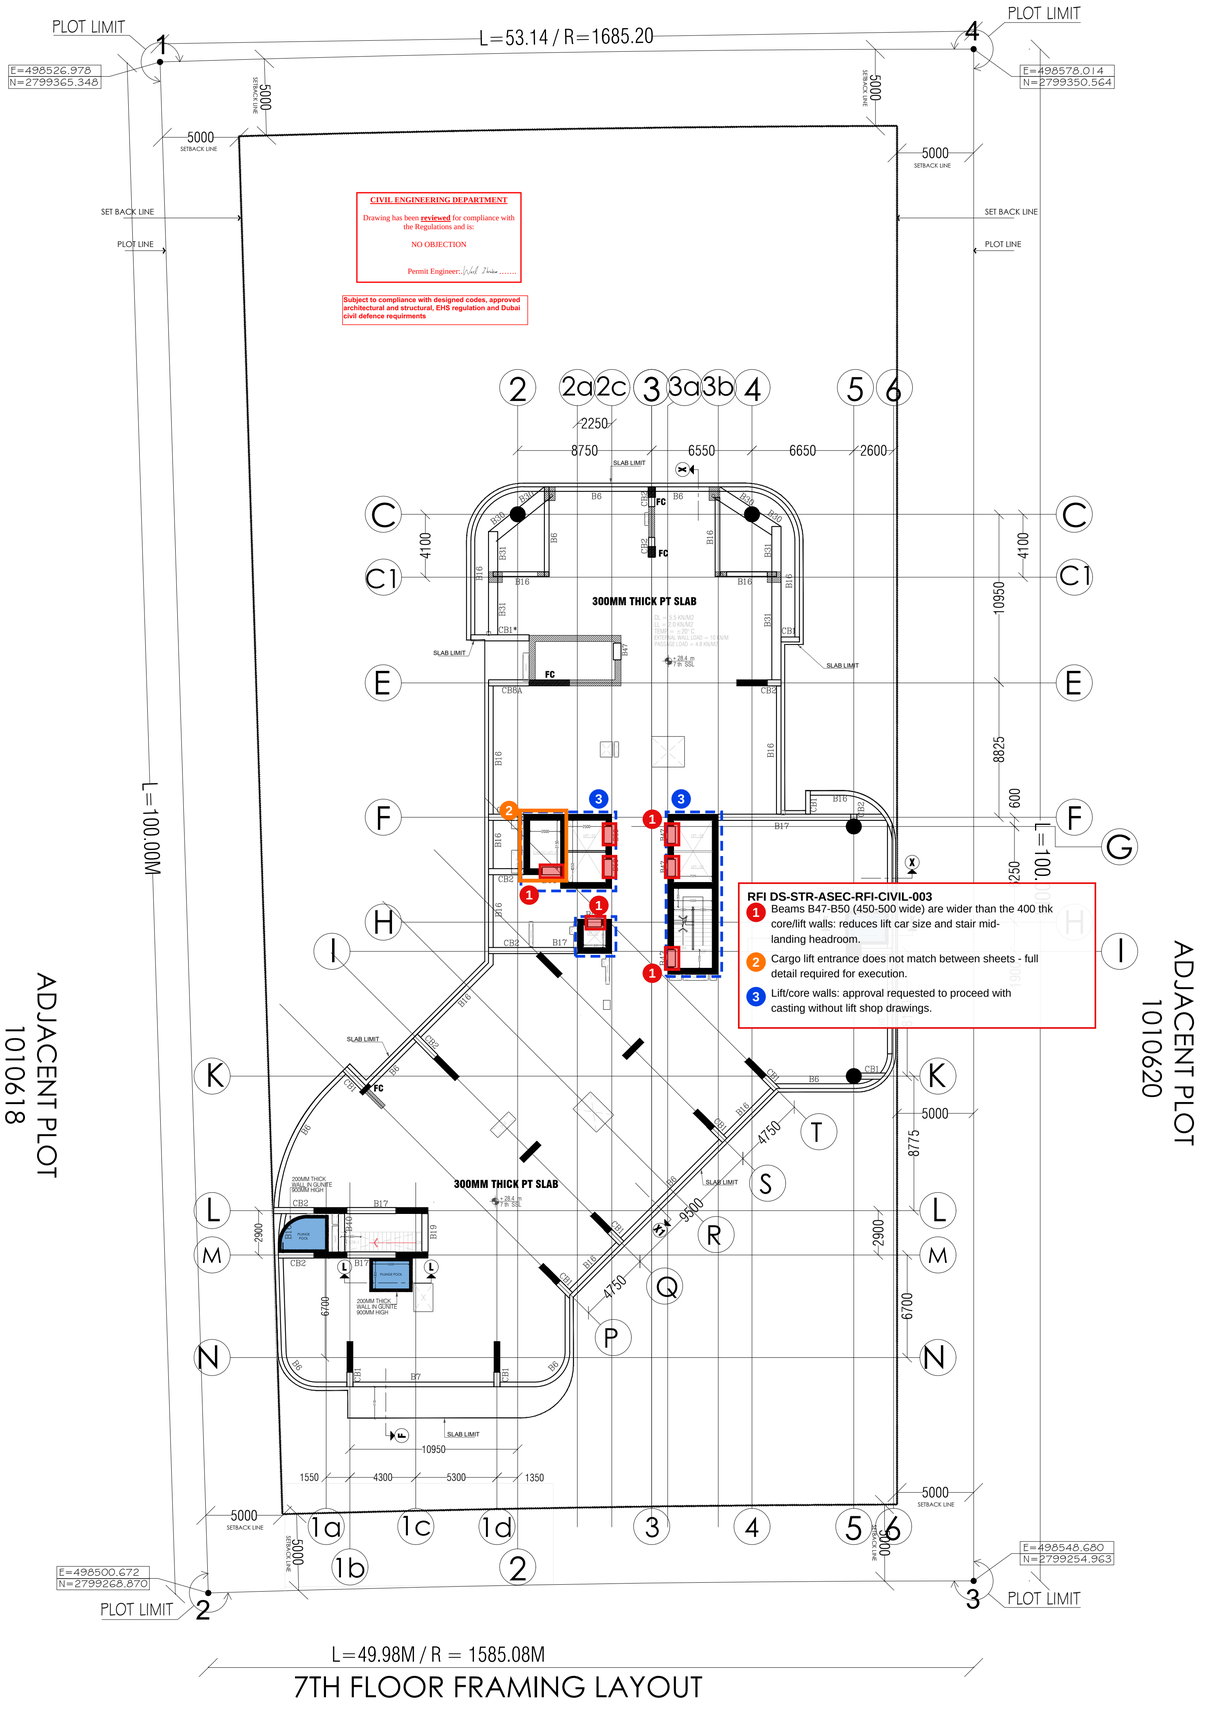

SCHEDULE OF BEAMS

	TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
	B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
	B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
	B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
	B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
	B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
	B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
	B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
	B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
	B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
	B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
	B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
	B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
	B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
	B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
	B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
	B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
	CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
	CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
	B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
	B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
	B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
	B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
	B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
	B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
	B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
	B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
	B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
	B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
	B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
	B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
	B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
	CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
	B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
	B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
	B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
	B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
	B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
	B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
	B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
	B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
	B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
	B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
	B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
	B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
	B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
	B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
1	B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
1	B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
1	B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
1	B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
	B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
	B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
	CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
	B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
	B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
	CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
	B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
	CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
	CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
	CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
	CB1A	600	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '*' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.











NOTE :

(1) THIS DRAWING IS THE PROPERTY OF :
AL SARAYA ENGINEERING CONSULTANT
P.O.BOX: 49162, DUBAI, U.A.E.
IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:
1. fcu = 50 N/mm²
2. fy = 460 N/mm²
* ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:
- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES :
- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG.
- WHEREVER NECESSARY BEAM DEPTH ARE INCREASED, INVERTED OR DOWNSTAND TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIMHERNAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS OR DRGS.

AL SARAYA ENGINEERING CONSULTANTS P.O.Box 49162 Dubai - U.A.E. Tel.: 04-3350084 Fax: 04-3350087

REVISIONS:

NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER:
B M L INVESTMENT LLC

OWNER:
DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT:
AL SARAYA ENGINEERING CONSULTANTS
السرايا للإستشارات الهندسية
Architects . Engineers . Planners P.O.Box - 49162 . DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT
CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, AIFI World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3866601
Fax: +971-4 3866602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101 | PLOT: 1010619

PROJECT:
PROPOSED B+G+7+R HOTEL ON PLOT NO.DIA-WE-0032(1010619), NAKHLAT DEIRA-101,DUBAI

DRG. TITLE:
7TH FLOOR FRAMING

SCALE:	1:150/A1	KEY:	–
APPROVED BY:	SJ	DRAWN BY:	SPP
DATE:	--	PLOTTED ON:	–
PRELIMINARY	FINAL	ADDITION	REVISION
ISSUED FOR:	–		

JOB NO. : 624

DRG. NO.: S-306

REV. 00

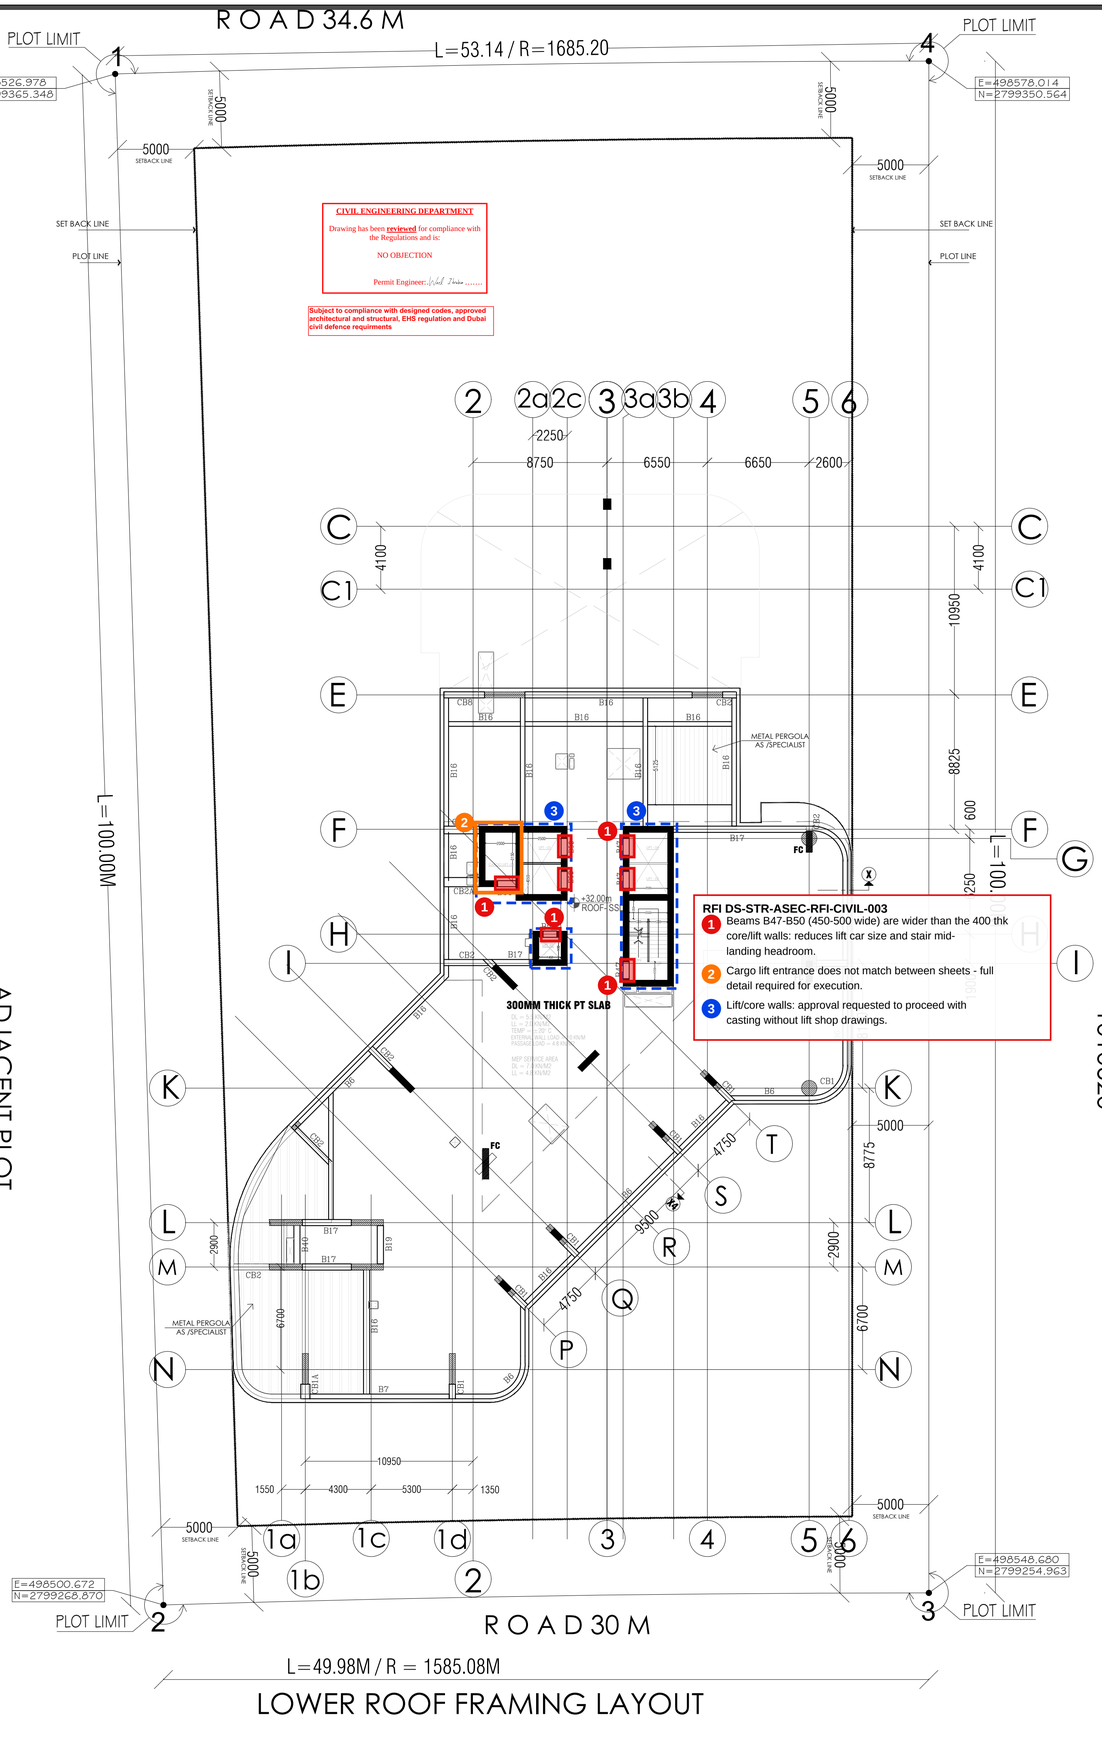

LOWER ROOF FRAMING LAYOUT

SCHEDULE OF BEAMS

TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
CB1A	600	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '•' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.



X1 TYP.SECTION
SCALE 1:50



X TYP.SECTION
SCALE 1:50



TYP.OPENING DETAILS
SCALE 1:50
TO USE 3T16 FOR OPENING WIDTH <1M,
3T20 FOR OPENING WIDTH >1M BUT<2M,
AND 3T25 FOR OPENING WIDTH >2M & UPTO 3M

NOTE :

(1) THIS DRAWING IS THE PROPERTY OF : AL SARAYA ENGINEERING CONSULTANT P.O.BOX: 49162, DUBAI, U.A.E. IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:

1. fcu = 50 N/mm²
2. fy = 460 N/mm²

★ ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:

- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES :
- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG
- WHENEVER NECESSARY BEAM DEPTH ARE INCREASED, MODIFIED OR DOWNSTAND TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIPHERAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS OR DRGS.

AL SARAYA ENGINEERING CONSULTANTS
المسرايا للاستشارات الهندسية
P.O.Box 49162 Tel.: 04-3350084
Dubai - U.A.E. Fax: 04-3350087

REVISIONS:

NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER: B M L INVESTMENT LLC

OWNER: DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT:
AL SARAYA ENGINEERING CONSULTANTS
السرايا للاستشارات الهندسية
Architects . Engineers . Planners P.O.Box - 49162 DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT
CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, AIFI World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602.
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101 | PLOT: 1010619

PROJECT:
PROPOSED B+G+7+R HOTEL
ON PLOT NO.DIA-WE-0032(1010619),
NAKHLAT DEIRA-101,DUBAI

DRG. TITLE:
LOWER ROOF FRAMING

SCALE:	1:150/A1	KEY:	–
APPROVED BY:	SJ	DRAWN BY:	SPP
DATE:	--	PLOTTED ON:	–
PRELIMINARY	FINAL	ADDITION	REVISION
ISSUED FOR:	–		

JOB NO. : 624

DRG. NO.: S-307

REV. 00

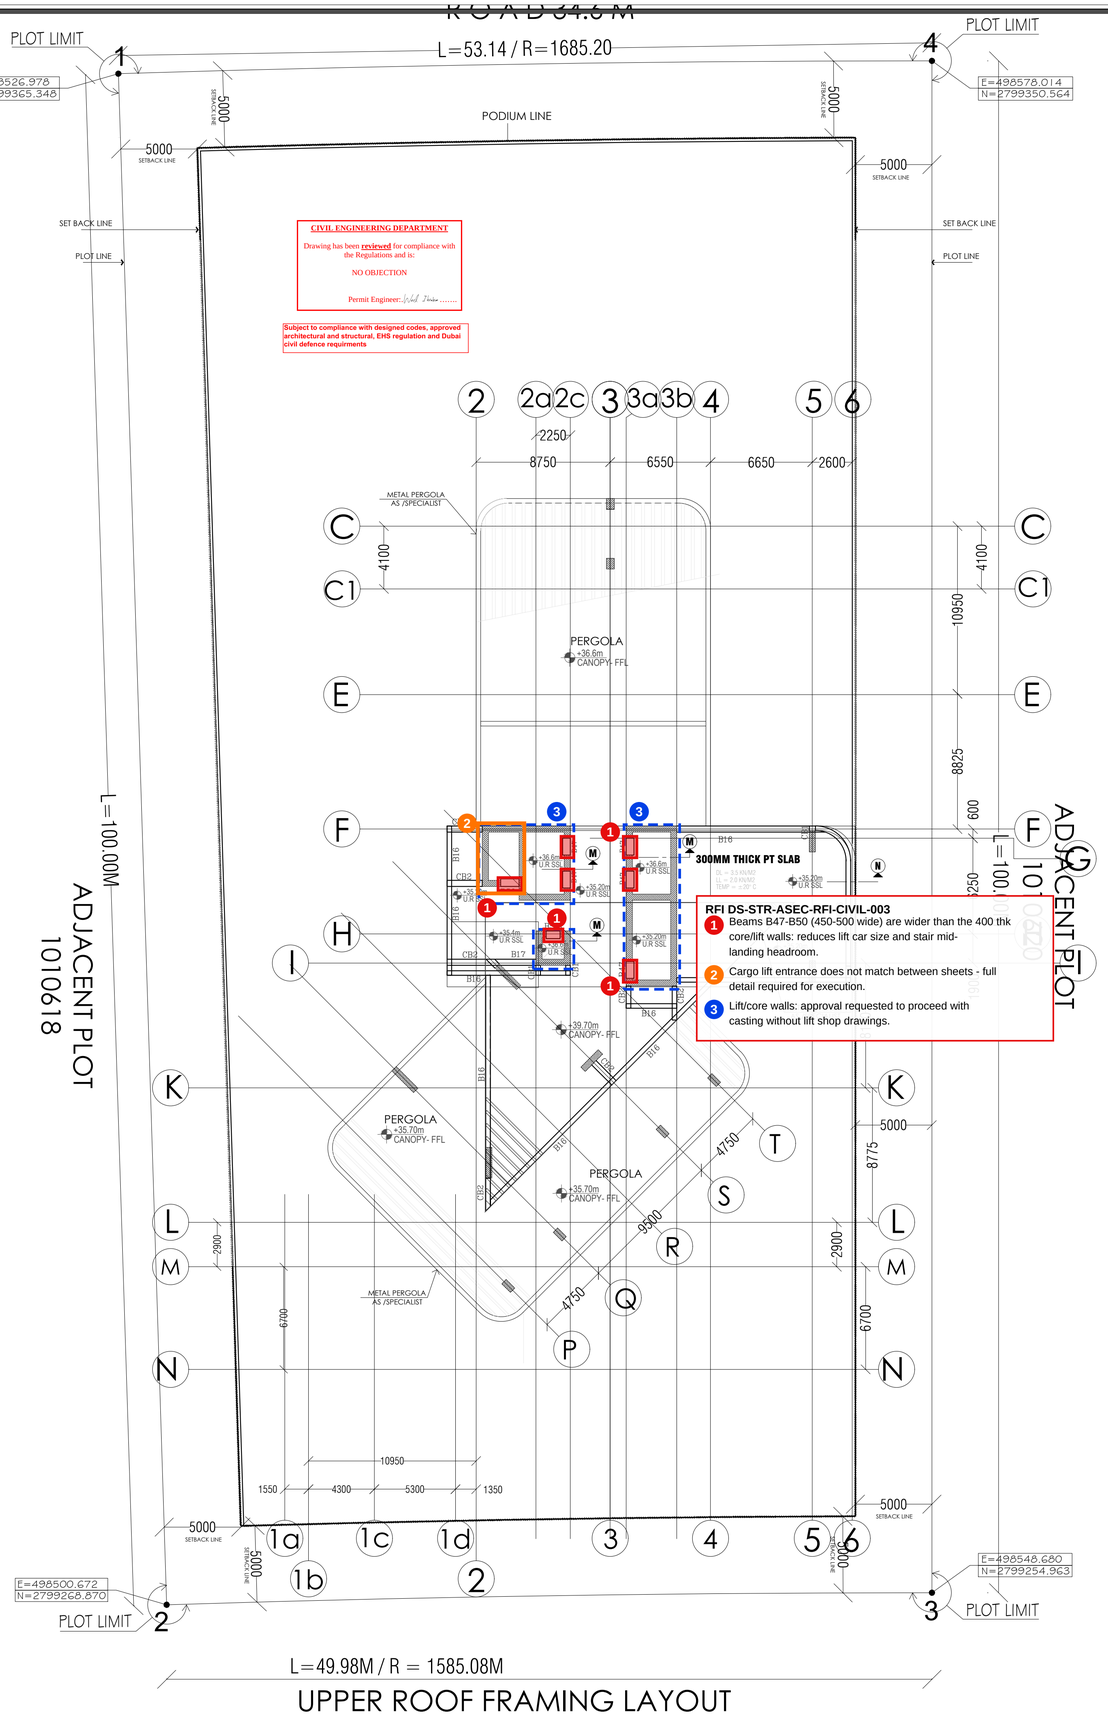

SCHEDULE OF BEAMS

TYPE	DIMENSION (mm.) WIDTH	DEPTH	BOTTOM REINFORCEMENT TROUGH	CURTAILED	TOP REINFORCEMENT TROUGH	EXTRA AT INTER.SUPP.	STIRRUPS (Spacing:mm)	SIDE FACE REBARS	REMARKS
B1/CB1*	500	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B2/CB2*	400	1200	4 T 32	2 T 32	4 T 32	3 T 25	4L-T10@ 200C/C	3 T 12	
B3/CB3	400	1200	5 T 32	2 T 32	5 T 32	4 T 32	4L-T10@ 200C/C	3 T 12	
B4	400	1200	4 T 32	1 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B5	400	1200	4 T 32	3 T 32	4 T 32	2 T 32	4L-T10@ 200C/C	3 T 12	
B6/CB6	300	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B7	300	750	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
B8/CB8	400	900	4 T 32	---	4 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B9	300	750	4 T 32	---	3 T 32	2 T 32	2L-T10@ 200C/C	---	
B10	500	1200	4 T 32	2 T 32	4 T 25	4 T 32	4L-T10@ 200C/C	3 T 12	
B11	300	350	3 T 25	---	3 T 25	---	2L-T10@ 200C/C	---	
B12	1400	1200	12 T 32	---	12 T 32	7 T 32	6L-T10@ 200C/C	3 T 12	
B13	800	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B14	600	1200	12 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B15	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 200C/C	3 T 12	
B16	300	750	2 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB1/B18	400	750	3 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	---	
CB2/B17	400	750	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	---	
B19	400	1200	3 T 32	---	3 T 32	---	2L-T10@ 200C/C	3 T 12	
B20	400	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B21	800	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B22	500	1200	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	3 T 12	
B23	1600	1400	16 T 32	6 T 32	8 T 32	8 T 25	12L-T12@ 100C/C	4 T 12	
B24	400	900	5 T 32	2 T 32	5 T 32	3 T 32	4L-T10@ 200C/C	2 T 12	
B25#/ CB25#	300	900 to 1600	4 T 32	---	2 T 32	2 T 32	2L-T10@ 200C/C	2 T 12	'#' mark shall have depth from bottom of ramp slab to ground floor top slab
B26	300	900	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	2 T 12	
B27	400	900	5 T 32	---	3 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B28	400	2400	4 T 32	---	4 T 32	2 T 32	4L-T12@ 200C/C	6 T 12	
B29	1400	1200	12 T 32	2 T 32	12 T 32	12 T 32	4L-T12@ 200C/C	6 T 12	
B30	1000	1200	12 T 32	---	12 T 32	12 T 32	6L-T12@ 200C/C	4 T 12	
B31	800	1200	10 T 32	---	10 T 32	4 T 32	6L-T12@ 200C/C	6 T 12	
CB32	400	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B33	600	900	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B34	800	750	6 T 32	---	6 T 32	2 T 32	4L-T12@ 200C/C	2 T 12	
B35/CB35	600	1550	6 T 32	---	6 T 32	6 T 32	4L-T12@ 200C/C	4 T 12	
B36	800	900	10 T 32	---	10 T 32	---	4L-T12@ 200C/C	2 T 12	
B37/CB37	300	1550	5 T 32	---	4 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B38/CB38	300	1550	4 T 32	---	4 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B39/CB39	400	1500	6 T 32	---	6 T 32	2 T 32	4L-T10@ 150C/C	4 T 12	
B40	400/300	600	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B41/CB41	450	2750	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B42/CB42	450	1400	2 T 32	---	2 T 32	---	2L-T10@ 150C/C	---	
B43	400	1800	2 T 32	---	2 T 32	---	2L-T10@ 200C/C	6 T 12	
B44	400	1800	2 T 32	---	2 T 32	---	4L-T10@ 125C/C	6 T 12	
B45	400	1800	2 T 32	---	2 T 32	---	4L-T12@ 125C/C	6 T 12	
B46	400	1800	3 T 32	---	3 T 32	---	4L-T10@ 125C/C	6 T 12	
B47	500	1400	4 T 32	---	4 T 32	2 T 32	4L-T10@ 200C/C	4 T 12	
B48	450	2750	5 T 32	---	5 T 32	---	4L-T10@ 200C/C	8 T 12	
B49	450	2750	3 T 32	---	3 T 32	---	4L-T10@ 200C/C	8 T 12	
B50	500	1400	3 T 32	---	3 T 32	---	4L-T12@ 200C/C	4 T 12	
B13A	800	1200	12 T 32	4 T 32	6 T 32	---	6L-T10@ 200C/C	4 T 12	
B36A	800	900	12 T 32	6 T 32	6 T 32	6 T 32	6L-T12@ 200C/C	2 T 12	
CB1*A	600	1200	6 T 32	---	6 T 32	4 T 32	4L-T12@ 200C/C	4 T 12	
B36B	1400	1200	16 T 32	8 T 32	16 T 32	16 T 32	10L-T12@ 100C/C	4 T 12	
B33A	800	1200	12 T 32	6 T 32	12 T 32	---	8L-T12@ 100C/C	4 T 12	
CB32A	600	1200	6 T 32	---	6 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
B23A	1800	1400	16 T 32	6 T 32	8 T 32	---	8L-T12@ 100C/C	4 T 12	
CB2A	400	750	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB8A	400	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 200C/C	4 T 12	
CB2B	500	900	4 T 32	1 T 32	4 T 32	3 T 32	4L-T10@ 100C/C	4 T 12	
CB1A	500	750	4 T 32	---	4 T 32	---	4L-T10@ 200C/C	4 T 12	

NOTE: 1) Beams with '##' mark to have depth to support lower slab at bottom at one end/side & higher slab at top at other end/side.
2) Beams with '#' mark shall have depth from parapet top of ramp to bottom of ramp slab.
3) Beams with '•' mark shall have depth of 1.95m
4) Width of any Beam supporting Floating Columns to be equal to Column width, Unless noted.



NOTE :

(1) THIS DRAWING IS THE PROPERTY OF : AL SARAYA ENGINEERING CONSULTANT P.O.BOX: 49162, DUBAI, U.A.E. IT IS NOT ALLOWED TO REPRODUCE ITS CONTENTS IN ANY FORM EXCEPT FOR THE PURPOSE FOR WHICH IT IS INTENDED.

(2) THIS DRAWING IS NOT TO BE SCALED. STATED DIMENSIONS ONLY ARE TO BE CONSIDERED. DIMENSIONS ARE IN CENTIMETERS ONLY.

(3) ANY DISCREPANCIES ARE TO BE BROUGHT TO THE ATTENTION OF THE ENGINEER AND RESOLVED BEFORE COMMENCEMENT OF ANY WORK.

NOTES:
1. fcu = 50 N/mm²
2. fy = 460 N/mm²
★ ALL THE SERVICE OPENINGS TO BE COORDINATED WITH ARCHITRCTURAL AND MEP DRAWINGS.

LEGEND:
- COLUMN CONTINUED TO TOP FLOOR
- COLUMN ENDING AT FLOOR LEVEL
- FLOATING COLUMN STARTING FROM FLOOR LEVEL

NOTES :
- BEAM SIZES SHOWN ARE MINIMUM REQUIRED HOWEVER SIZE SHALL BE INCREASED TO SUIT ARCHITECTURAL DETAILS AS SHOWN IN RESPECTIVE WALL SECTIONS IN ARCH DWG
- WHEREVER NECESSARY BEAM DEPTH ARE INCREASED, INVERTED OR DOWNSTAND TO SUIT ARCHITECTURAL WALL SECTION, ELEVATIONAL TREATMENT, PROJECTION ,CONTRACTOR TO COORDINATE
- CONTRACTOR TO CO-ORDINATE ALL ARCHITECTURAL PROJECTIONS, ELEVATIONAL TREATMENT, VARIOUS LEVEL DIFFERENCES ETC.
- CONTRACTOR TO PREPARE THE SHOP DRAWINGS FOR BLOCKWALL LAYOUT ALONG WITH EDGE & INTERMEDIATE STIFFENER COLUMN NECESSARY HOLDFAST & ACCESSORIES CONNECTION OF BLOCK WORK WITH RC ELEMENTS VERTICALLY & HORIZONTALLY.
- CONTRACTOR TO SEE ALL THE PERIPHERAL BEAMS SHALL BE WELL CO-ORDINATED WITH ARCHITECTURAL LEVELS OR DROS.

AL SARAYA ENGINEERING CONSULTANTS P.O.Box 49162 Dubai - U.A.E. Tel.: 04-3350084 Fax: 04-3350087

REVISIONS:		
NO.	DESCRIPTION:	DATE:
00	FOR TENDER	---
01	FOR APPROVAL	13.01.25
02	FOR BP APPROVAL	24.04.25
03	FOR BP APPROVAL	16.06.25
04		

DEVELOPER: B M L INVESTMENT LLC

OWNER: DUBAI ISLANDS L.L.C

DESIGNER:

CONSULTANT: AL SARAYA ENGINEERING CONSULTANTS السرايا للإستشارات الهندسية
Architects . Engineers . Planners P.O.Box - 49162 . DUBAI, U.A.E.
Tel 04-3350084 Fax 04-3350087 E-mail :sarayadx@emirates.net.ae

SUSTAINABLE & MEP CONSULTANT: CONSISTENT ENGINEERING CONSULTANTS
Post Box No: 125786, Office 2001 & 2002, AIFI World Tower, Sheikh Zayed Road, Opp. World Trade Centre, Dubai.
Tel: +971-4 3860601
Fax: +971-4 3860602
Email: info@consistentconsultants.com
Website: consistentconsultants.com

COMMUNITY: NAKHLAT DEIRA-101	PLOT: 1010619
PROJECT:	PROPOSED B+G+7+R HOTEL ON PLOT NO.DIA-WE-0032(1010619), NAKHLAT DEIRA-101,DUBAI
DRG. TITLE:	UPPER ROOF FRAMING
SCALE: 1:150/A1	KEY: –
APPROVED BY: SJ	DRAWN BY: SPP
DATE: --	PLOTTED ON: –
PRELIMINARY / FINAL / ADDITION / REVISION	
ISSUED FOR: –	
JOB NO. : 624	
DRG. NO.: S-308	REV. 00
